

Pitcaple Timber Signal Box Network Rail Demolition



Commercial Property Maintenance Services Ltd

DEMOLITION OF REDUNDANT SIGNAL BOX

CPMS were awarded a contract by Network Rail to demolish the redundant Pitcaple timber Signal Box using a NFDC sub contractor.


The project comprised of the following elements:-

- Liaising with local residents to minimise disruption and also to secure access onto site.
- The Demolition of the lineside structure was undertaken during a Saturday night line blockage.
- Works utilised a long-reach excavator to minimise the need to remove existing mature vegetation and trees.
- Segregation, removal and re-cycling of all debris from site.
- Top-soiling of Signal Box site to allow vegetation to recover the area.
- Reinstatement of line side boundary fencing.
- All works completed on time and budget with no issues.



Signal Box prior to demolition with a green fibre optic cable present in the cess of the track.

Delivered with minimal disturbance to line side neighbours or wildlife.

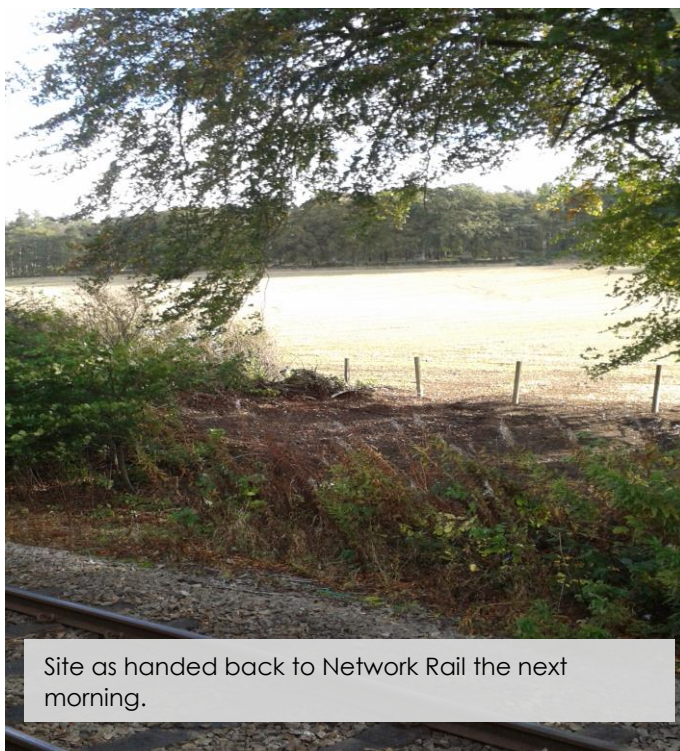

Site as handed back to Network Rail the next morning.
